



SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# UPDATE ON MEASURES L AND X PROJECTS

October 23, 2019

San Mateo-Foster City School District  
Presentation to the Citizens' Bond Oversight Committee

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT



SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

**BOND OVERSIGHT COMMITTEE MEASURE X**  
*(with oversight on remaining Measure L Projects)*

**PLACE:** SAN MATEO-FOSTER CITY SCHOOL DISTRICT  
1170 CHESS DRIVE, FOSTER CITY, CA 94404  
BOARD ROOM

**DATE:** October 23, 2019

**TIME:** 5:30 – 7:00 PM OPEN SESSION, BOARD ROOM

---

1. Call to Order
2. Roll Call
3. Review of Agenda
4. Public Comment – Anyone wishing to address the CBOC may do so at this time.
5. Approval of Meeting Minutes from May 9, 2019 and July 31, 2019
6. Selection of CBOC Officers  
CBOC Chair  
CBOC Vice Chair
7. Review of Financial Expenditures
8. Measure L & X Program Status Update - Facilities Project Managers
9. Next Meeting and Tentative Future Meeting Schedule
10. Future Agenda Items
11. Adjourn

**Attachments**

- A. Measure L Financial Reports as of 30 September 2019
- B. Measure X Financial Reports as of 30 September 2019





# CURRENT MEASURE L & MEASURE X PROJECTS

## ■ MEASURE L PROJECTS

- ◆ San Mateo Park Elementary School Security Fencing (Bob Price)
- ◆ Borel Middle School Security Fencing (Bob Price)
- ◆ Abbott Middle School Roofing (Mark Sherrill)
- ◆ Abbott Middle School Shade Structure (Mark Sherrill)
- ◆ George Hall Elementary School Roofing (Alex Kristal)
- ◆ George Hall Elementary School Shade Structure (Alex Kristal)

## ■ MEASURE X PROJECTS

- ◆ New Elementary School in Foster City (Kevin Sanders)
- ◆ Bayside Academy Gym (Kevin Sanders)
- ◆ Abbott Middle School Gym and Classrooms (Mark Sherrill)
- ◆ Borel Middle School Phase I & II Site Work and Classrooms (Bob Price)
- ◆ Borel Middle School Phase III Gym (Bob Price)





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# SAN MATEO PARK FENCING MEASURE L

**Contractor: Crusader Fence**

**Contractor: American Asphalt**

**Board Approved Date: Crusader Fence: April 20, 2017 & American Asphalt: May 8, 2018**

**Contract Amount: Crusader Fence \$165,000 & American Asphalt \$544,444**

## **Project Schedule & Milestones**

- ◆ Demolition – Spring Break 2019 and Remainder Summer 2019
- ◆ Front Stairs and Walkway – Spring Break 2019
- ◆ Ramp and Walkway by Multipurpose Room – Summer 2019
- ◆ Front of Multi-Purpose Room – Summer 2019
- ◆ Anticipated Completion – Fall 2019

**CBOC Presentation October 23, 2019**





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# SAN MATEO PARK FENCING MEASURE L



COMPLETED ORNAMENTAL FENCING IN FRONT OF MULTI PURPOSE BUILDING

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# SAN MATEO PARK FENCING MEASURE L



COMPLETED ORNAMENTAL FENCING LOOKING TOWARDS ADMIN. BUILDING

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# SAN MATEO PARK FENCING MEASURE L



NEW ORNAMENTAL FENCING ENCLOSING AREA IN FRONT OF ADMINISTRATION AND CLASSROOM

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# SAN MATEO PARK FENCING MEASURE L



EXTERIOR TALLER FENCING AND SMALLER FENCING AT WALKWAY

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# SAN MATEO PARK FENCING MEASURE L



SMALLER FENCING AT WALKWAY IN FRONT OF ADMINISTRATION

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# SAN MATEO PARK FENCING MEASURE L



ORNAMENTAL FENCING AT FRONT OF SCHOOL ON CLARK DRIVE

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL MIDDLE SCHOOL FENCING MEASURE L

**Contractor: Crusader Fence**

**Contractor: American Asphalt**

**Board Approved Date: Crusader Fence: April 20, 2017 & American Asphalt: May 8, 2018**

**Contract Amount: Crusader Fence \$66,000 & American Asphalt \$473,895**

## **Project Schedule & Milestones**

- ◆ Remaining concrete steps placed – Summer 2019
- ◆ Chair lift installed – December 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL MIDDLE SCHOOL FENCING MEASURE L



ORNAMENTAL FENCING WITH AUTOMATIC GATE AT BACK PARKING LOT


CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL MIDDLE SCHOOL FENCING MEASURE L

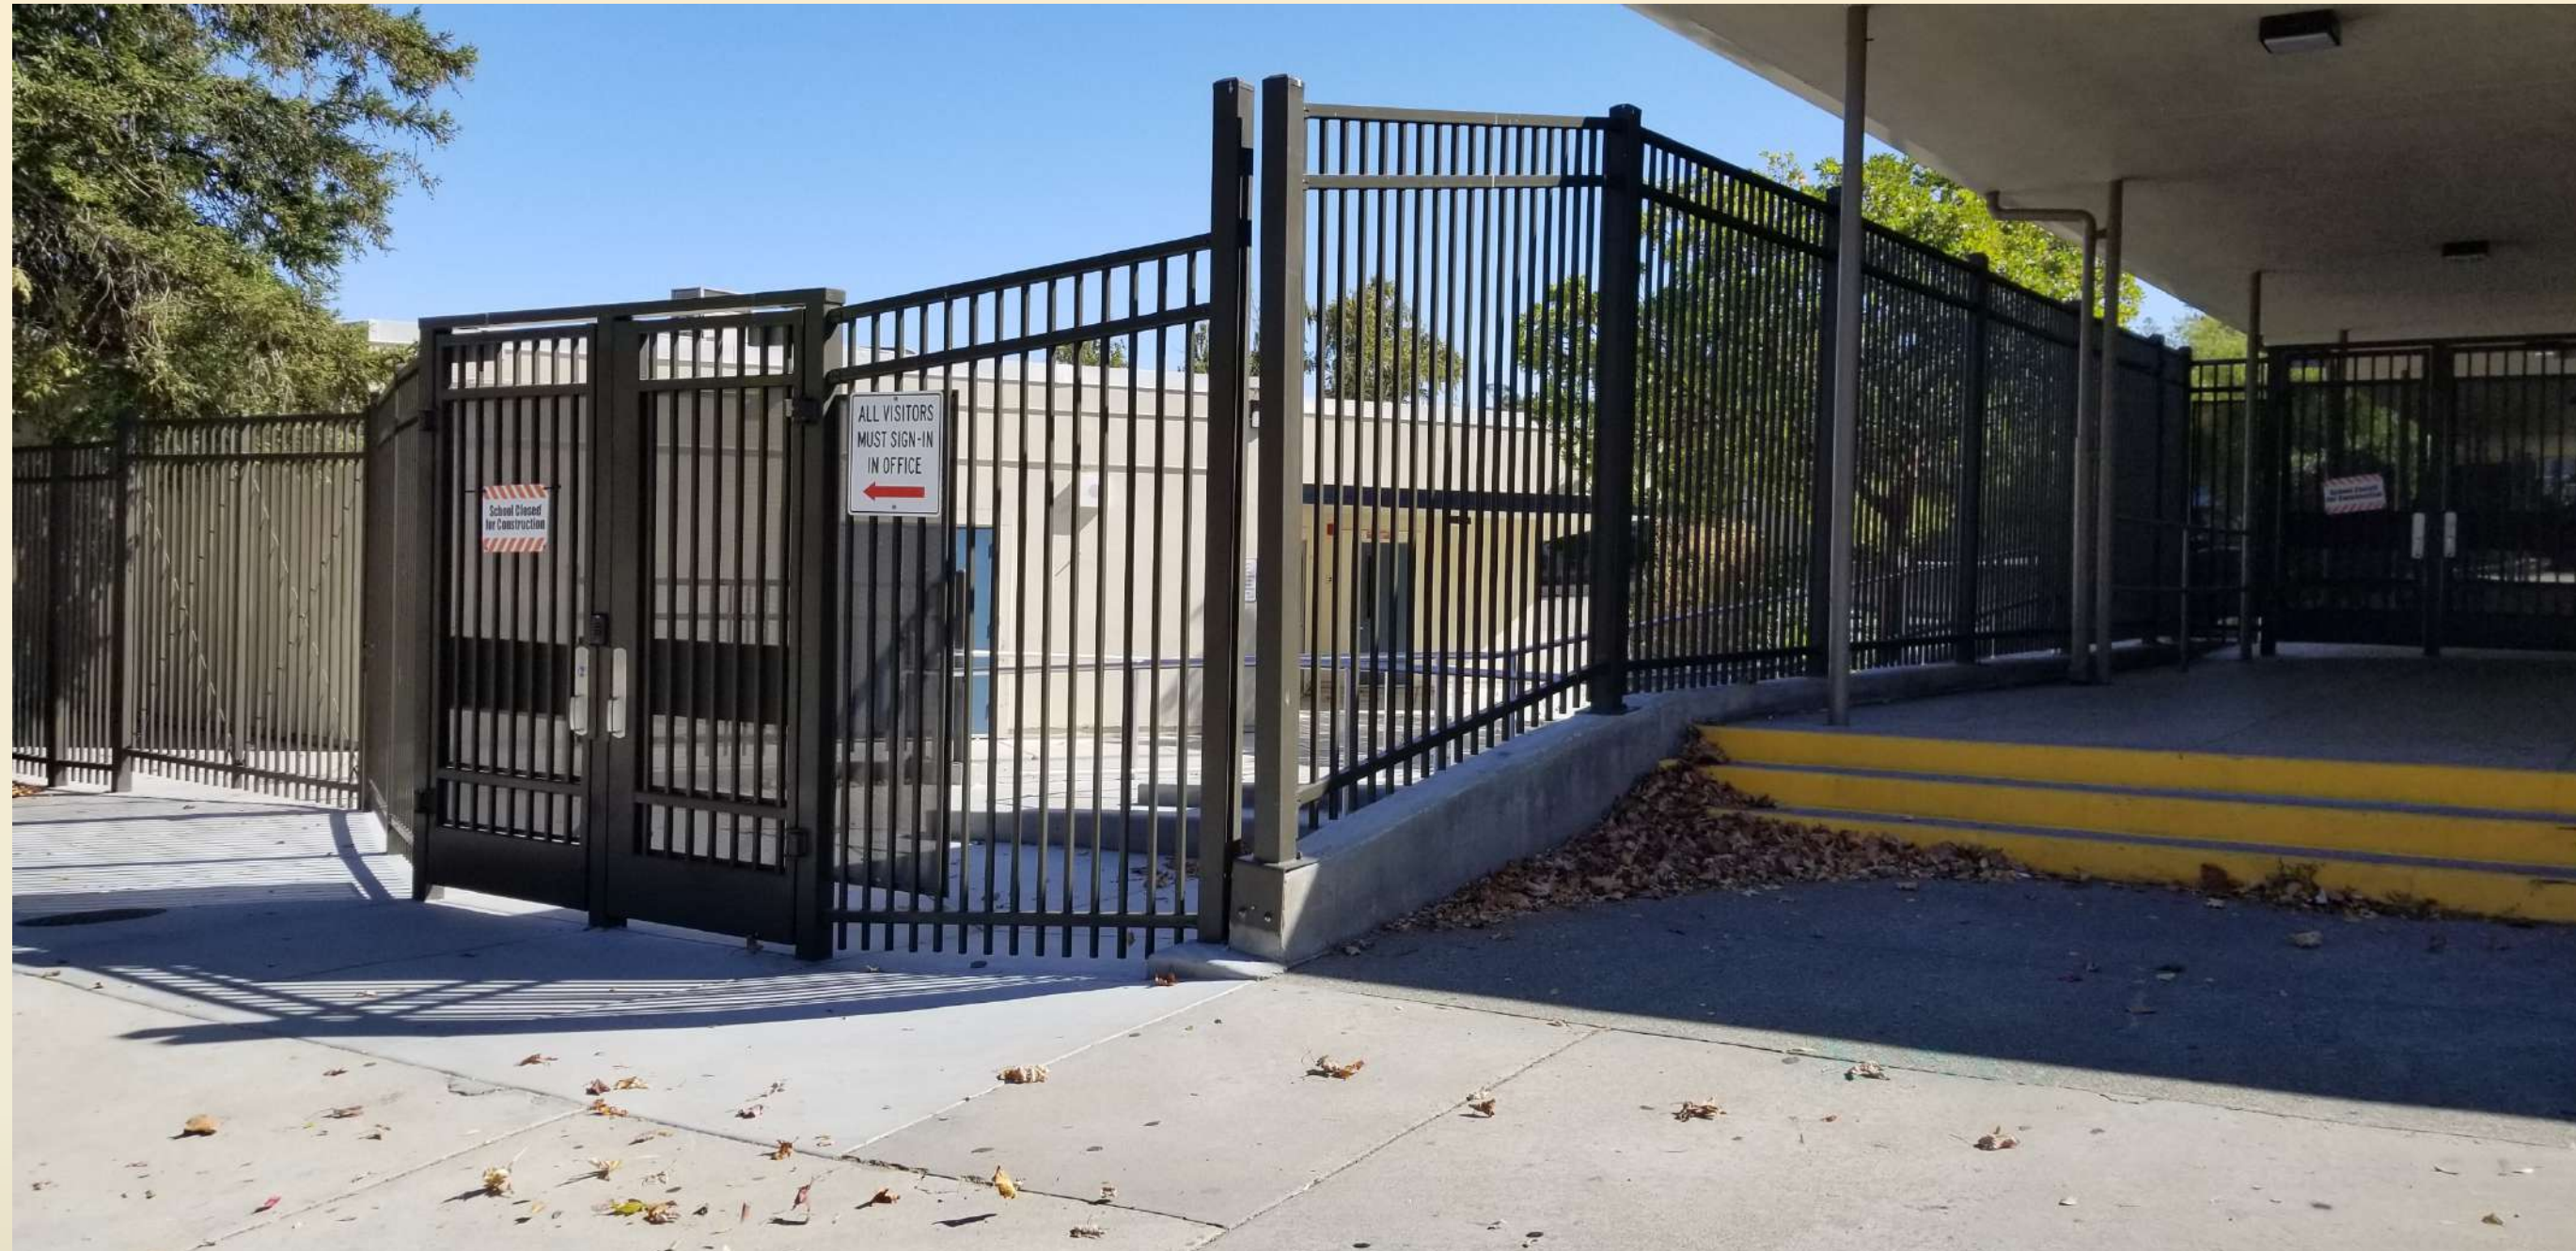

ORNAMENTAL FENCING AT EXISTING MPR ON BARNESON

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL MIDDLE SCHOOL FENCING MEASURE L



ORNAMENTAL FENCING ALONG FRONT OF SCHOOL AT BARNESON

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL MIDDLE SCHOOL FENCING MEASURE L



NEWLY CONSTRUCTED STAIRS, WHEELCHAIR LIFT TO BE INSTALLED

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL MIDDLE SCHOOL FENCING MEASURE L



NEWLY CONSTRUCTED STAIRS, CHAIRLIFT TO BE MOUNTED ON STAIRS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL MIDDLE SCHOOL FENCING MEASURE L



NEWLY CONSTRUCTED STAIRS, CHAIRLIFT TO BE MOUNTED ON STAIRS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL MIDDLE SCHOOL FENCING MEASURE L



WHEELCHAIR LIFT TO BE MOUNTED ON STAIRS, TO BE COMPLETED BY DECEMBER

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL ROOFING MEASURE L

**Contractor: Andy's Roofing**

**Board Approved Date: March 7, 2019**

**Contract Amount: \$733,300.00**

## **Project Schedule & Milestones**

### Demolition

- Wing C / 3 April 2019
- Wing A / 1 & B/2 Summer 2019

### Installation

- Wing C / 3 April 10, 2019
- Wing A / 1 and Gym July 20, 2019
- Wing B / 2 August 10, 2019

**CBOC Presentation October 23, 2019**





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL ROOFING MEASURE L



ROOF DEMOLITION WING 3

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL ROOFING MEASURE L



TYPICAL SHINGLE ROOF TO BE INSTALLED AT ALL ROOFS, EXCEPT PORTABLES

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL ROOFING MEASURE L



WING 3 SHINGLE ROOF INSTALLATION IN PROGRESS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL ROOFING MEASURE L



PORTABLE ROOFS TO RECEIVE NEW COATING

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL ROOFING MEASURE L



COMPLETED ROOF COATING AT PORTABLE ROOF

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL SHADE STRUCT. MEASURE L

**Contractor: Community Playgrounds Inc.**

**Board Approved Date: June 20, 2019**

**Contract Amount: \$239,063.80**

## **Project Schedule & Milestones**

- ◆ Ramp to shade Structure completed August 10, 2019
- ◆ Shade Installation start October 1, 2019
- ◆ Anticipated Completion - Spring 2020

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL SHADE STRUCT. MEASURE L



GRADING FOR NEW RAMP LEADING TO THE GROVE WHERE THE SHADE STRUCTURE WILL BE INSTALLED.  
RAMP COMPLETED AUGUST 10, 2019

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL SHADE STRUCT. MEASURE L



RAMP LEADING TO LUNCH GROVE COMPLETED AUGUST 10, 2019

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL SHADE STRUCT. MEASURE L



PREPARATION OF GATES OF THE SECURITY FENCING LEADING TO RAMP

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL SHADE STRUCT. MEASURE L



SECURITY FENCE GATE INSTALLATION

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL SHADE STRUCT. MEASURE L



COMPLETED RAMP TO LUNCH GROVE WHERE THE SHADE STRUCTURE WILL BE INSTALLED.

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT MIDDLE SCHOOL SHADE STRUCT. MEASURE L



COMPLETED RAMP/STAIR FOR ACCESS TO LUNCH GROVE

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL SHADE STRUCTURE MEASURE L

**Contractor: Community Playgrounds, Inc.**

**Board Approved Date: June 6, 2019**

**Contract Amount: \$128,893.00**

## **Project Schedule & Milestones**

- ◆ Demolition – July 8, 2019
- ◆ Dug for Column Foundations – July 15, 2019
- ◆ Foundations Concrete Poured – July 22, 2019
- ◆ Frame Assembly – July 29, 2019
- ◆ Completed – August 9, 2019

**CBOC Presentation October 23, 2019**



# GEORGE HALL SHADE STRUCTURE MEASURE L



EXISTING LUNCH COURTYARD PRIOR TO SHADE STRUCTURE INSTALLATION





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL SHADE STRUCTURE MEASURE L



ASSEMBLY OF STEEL FRAMES FOR THE SHADE STRUCTURE

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL SHADE STRUCTURE MEASURE L



COMPLETED SHADE STRUCTURE WITH LIGHTING

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL SHADE STRUCTURE MEASURE L



COMPLETED SHADE STRUCTURE WITH LIGHTING

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL SHADE STRUCTURE MEASURE L



CELEBRATING THE SHADE STRUCTURE OPENING WITH A RIBBON CUTTING CEREMONY

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL ROOFING MEASURE L

**Contractor: State Roofing Systems, Inc**  
**Board Approved Date: March 21, 2019**  
**Contract Amount: \$618,622.00**

## **Project Schedule & Milestones**

- ◆ Project Started - June 23, 2019
- ◆ Demolition - July 8, 2019
- ◆ Wing A or 1 - July 16, 2019
- ◆ Wing B or 2 - July 26, 2019
- ◆ Wing C or 3 - July 19, 2019
- ◆ Wing D or 4 - August 2, 2019
- ◆ Portables - August 7, 2019
- ◆ Completed – August 7, 2019

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL ROOFING MEASURE L



TYPICAL ROOFING INSTALLATION AT WINGS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL ROOFING MEASURE L



COMPLETED ROOF INSTALLATION AT FOREGROUND AND AT RIGHT.

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL ROOFING MEASURE L



COMPLETED ROOF INSTALLATION AT WING 3

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# GEORGE HALL ROOFING MEASURE L



COMPLETED ROOF INSTALLATION AT WING 2

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# MEASURE X PROJECTS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# NEW ELEMENTARY SCHOOL IN FOSTER CITY MEASURE X

**Contractor: Rodan Builders**

**Board Approved Date: June 6, 2019**

**Contract Amount: \$29,998,000.00**

## **Project Schedule & Milestones**

- ◆ Next Milestone – Building B1, B2, C and A footings, October, 2019
- ◆ Next Milestone – Building B1, B2, C, and A Slabs December, 2019
- ◆ Next Milestone – Building Steel B1, B2, C and A, February 2020
- ◆ Anticipated Completion – Beginning of 2021

**CBOC Presentation October 23, 2019**





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# NEW ELEMENTARY SCHOOL IN FOSTER CITY MEASURE X



UNDERGROUND ELECTRICAL

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# NEW ELEMENTARY SCHOOL IN FOSTER CITY MEASURE X



MAIN ELECTRICAL FEEDERS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# NEW ELEMENTARY SCHOOL IN FOSTER CITY MEASURE X



BUILDING FOOTINGS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# NEW ELEMENTARY SCHOOL IN FOSTER CITY MEASURE X



BUILDING FOOTING POUR B2

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# NEW ELEMENTARY SCHOOL IN FOSTER CITY MEASURE X



CONCRETE BOOM B1, B2

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BAYSIDE ACADEMY NEW GYM MEASURE X

**Contractor: Rodan Builders**

**Board Approved Date: 3/21/2019**

**Contract Amount: \$9,896,000.00**

## **Project Schedule & Milestones**

- ◆ Next Milestone – November, 2019 - Install exterior doors and frames.
- ◆ Next Milestone – December, 2019 - Finish Building Exterior / Water Tight.
- ◆ Next Milestone – January, 2020 - Install HVAC Units on Gym Roof.
- ◆ Next Milestone – January, 2020 - Continue interior rough-in for Plumbing, HVAC, and Electrical
- ◆ Anticipated Completion – April, 2020

**CBOC Presentation October 23, 2019**





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BAYSIDE ACADEMY NEW GYM MEASURE X



MAIN GYM LOBBY

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BAYSIDE ACADEMY NEW GYM MEASURE X



NEW MAIN LOBBY RESTROOMS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BAYSIDE ACADEMY NEW GYM MEASURE X



MAIN GYM

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BAYSIDE ACADEMY NEW GYM MEASURE X



EXTERIOR OF NEW GYM

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BAYSIDE ACADEMY NEW GYM MEASURE X



Timelapse Video

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT NEW GYM & CLASSROOMS MEASURE X

**Contractor: Rodan Builders Inc.**

**Board Approved Date: March 21, 2019**

**Contract Amount: \$15,781,000.00**

## **Project Schedule & Milestones**

- ◆ Gym Building Steel Raised – November, 2019
- ◆ Stairs From Parking to Gym Level – January, 2020
- ◆ Elevator – May, 2020
- ◆ Shade Structure (Measure L) – May, 2020
- ◆ Anticipated Completion – July, 2020

**CBOC Presentation October 23, 2019**





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT NEW GYM & CLASSROOMS MEASURE X



LOBBY

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT NEW GYM & CLASSROOMS MEASURE X



LOCKER ROOMS AND CLASSROOMS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT NEW GYM & CLASSROOMS MEASURE X



BACK OF LOCKER ROOMS, CLASSROOM BUILDING

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT NEW GYM & CLASSROOMS MEASURE X



FROM THE GYM LOOKING AT THE LOBBY

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT NEW GYM & CLASSROOMS MEASURE X



FROM THE GYM LOOKING AT THE LOCKER ROOMS AND CLASSROOMS

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# ABBOTT NEW GYM & CLASSROOMS MEASURE X



Timelapse Video

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE I AND II MEASURE X

**Contractor: Rodan Builders, Inc. (PHASE I) & American Modular Service, Inc. (Phase II)**

**Board Approved Date: January 25, 2018 & February 21, 2019**

**Contract Amount: \$1,851,240 & \$6,506,000**

## **Project Schedule & Milestones**

- ◆ Modular Classroom Occupancy – January, 2020
- ◆ Site Work Completion – July, 2020
- ◆ Anticipated Completion – August 7, 2020

**CBOC Presentation October 23, 2019**





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE I AND II MEASURE X



BIO SWALE FROM UPPER PLAZA TO LOWER YARD

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE I AND II MEASURE X



NEW RAMP FROM SCIENCE BUILDING TO NEW CLASSROOM COURTYARD

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE I AND II MEASURE X



EMERGENCY VEHICLE ACCESS TO NEW ADDITION

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE I AND II MEASURE X



FOUR CLASSROOM CLUSTER MODULAR BUILDING

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE I AND II MEASURE X



COURTYARD BETWEEN THE CLASSROOM BUILDINGS LEADING TO GYM

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE I AND II MEASURE X



TYPICAL CLASSROOM INTERIOR

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE I AND II MEASURE X



TYPICAL CLASSROOM INTERIOR

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE I AND II MEASURE X



Timelapse Video

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE III – GYM BUILDING MEASURE X

**Contractor: Beals Martin, Inc.**

**Board Approved Date: August 22, 2019**

**Contract Amount: \$10,237,159**

## **Project Schedule & Milestones**

- ◆ Anticipated Completion – November, 2020





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE III – GYM BUILDING MEASURE X



UTILITY TRENCH

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# BOREL NEW GYM & CLASSROOMS PHASE III – GYM BUILDING MEASURE X



Borel Gym Underground Utility Trenching

CBOC Presentation October 23, 2019





SAN MATEO-  
FOSTER CITY  
SCHOOL DISTRICT

# QUESTIONS/COMMENTS?

CBOC Presentation October 23, 2019
